

Work Order ID 131760

Tuesday, April 21, 2015 1:49:21 PM

131760

Page 1

Item ID: D4020-11 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: End Mesh, Basket
 Start Date: 4/20/15 Start Qty: 8.00 ***8*** Cust Item ID:
 Required Date: 4/20/15 Req'd Qty: 8.00 ***8*** Customer:
 Reference:

Approvals: Process Plan: MCS Date: 15-04-22 Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D4020	A								

100 FLOW WATER JET 0.00
100 Waterjet 8 0 JM15-5-1

FLOW CNC Waterjet
 SS MESH.

Memo
 1-Cut as per Dwg D4020
 Dwg Rev: A
 Prog Rev: A
 2-Deburr if necessary

110 QC2- Inspect parts off machine FAI/FAIB 0.00
110 QC 8 0 JM15-5-1

Quality Control

Memo
 CUT OUTS WILL BE CUT BY WELDERS WHEN INSTALL ON BASKET

120 QC8- Inspect parts - second check 0.00
120 QC 2 0

Quality Control

Memo
 CUT OUTS WILL BE CUT BY WELDERS WHEN INSTALL ON BASKET

DAG
 38
 9-89

MAY 01 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause			FAULT CATEGORY		
Environment	☐	No Re-verification	☐	Pressure/Forced	☐
Design	☐	Operator	☐	Bending	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐
Material	☐	Use for Testing	☐	Cuffs	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐
Past Expiry Date	☐	Manufacturing Process	☐		
Misidentified	☐	Past Due	☐	OTHER :	

Tuesday, April 21, 2015 2:05:58 PM

131819

Page 1

Accept

N900040100

Setup Start *NS1*

Revision ID:

Item Name: Adapter

Stop *NS2*

Start Date: 4/20/15 **Start Qty:** 2.00

?

Cust Item ID:

Required Date: 4/20/15 **Req'd Qty:** 2.00

~

Customer:

Reference:

Approvals: Process Plan: CZ Date: 15/04/22 Tooling: _____ Date: _____

Run Start *NR1*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop *NR2*

[illegible]

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : ☐					

Work Order ID 131819

Tuesday, April 21, 2015 2:05:58 PM

131819

Page 2

Item ID: D3573-1 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Adapter
Start Date: 4/20/15 Start Qty: 2.00 ***2*** Cust Item ID:
Required Date: 4/20/15 Req'd Qty: 2.00 ***2*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
130	QC8- Inspect parts - second check	0.00							
130									
QC	Memo	0.00							DAS 08 9-89
Quality Control									
140	Chemical Conversion Coat per QSI005 4.1	0.00							
140									
HandFinish	Memo	0.00							
Hand Finishing									
150	Grey Sandtex(Ref:4.3.5.6) per QSI005 4.3	0.00							
150									
Powdercoat	Memo	0.00							
Powder Coating									
	START TIME: <u>11:40</u> OVEN TEMPERATURE:								
	FINISH TIME: <u>12:10</u>								

D.A 15/05/07

2 0

15-5-13

2 0 15-5-13

2 0 15-5-20

DAS
34
9-89

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width: 100%; border: none;"> <tr> <td style="width: 15%;">Skid-tube ☐</td> <td style="width: 15%;">Cross tube ☐</td> <td style="width: 15%;">Water Jet ☐</td> <td style="width: 15%;">Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																						
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																						
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																						
Large Fab ☐	Composite ☐	Supplier ☐																							
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval																		
Description Work Order Deviation				Disposition				Completed By																	
								Lead hand / Supervisor Approval Verification																	
										QC / QA Coordinator Approval															
Root Cause		FAULT CATEGORY																							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐																				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐																				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐																				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐																				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐																				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐																				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐																				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐																				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐																				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐																				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :																							
Misidentified ☐	Past Due ☐																								

Work Order ID 131819

Tuesday, April 21, 2015 2:05:58 PM

131819

Page 3

Item ID: D3573-1 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Adapter
 Start Date: 4/20/15 Start Qty: 2.00 ***2*** Cust Item ID:
 Required Date: 4/20/15 Req'd Qty: 2.00 ***2*** Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
160 *160* QC Quality Control	QC3- Inspect Part Finish Memo	0.00 0.00				<u>(2)</u>			DAS 38 9-89 MAY 20 2015
170 *170* Packaging Packaging	Identify as per dwg & Stock Location: <u>GA</u> Memo LOCATION : GA	0.00 0.00				<u>2</u>			DAS 27 9-89 MAY 21 2015
180 *180* QC Quality Control	QC21- Final Inspection - Work Order Release Memo	0.00 0.00				<u>MLJ</u>			MAY 21 2015

MLJ MAY 21 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

Picklist Print

Tuesday, April 21, 2015 2:05:58 PM

Page 1

Work Order ID: 131819

131819

Parent Item: D3573-1

D3573-1

Parent Item Name: Adapter

Start Date: 4/20/15

Required Date: 4/20/15

Start Qty: 2.00

Required Qty: 2.00

Comments: IPP Rev:A New Issue 07-01-29 JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M6061T6B0.625X02.50 0		Purchased	No			100	f	14.7700	0.292	1			

M6061T6B0 625X02 500

6061-T6 Bar .625 x 2.50

15-5-6

Location

Loc Qty

Loc Code

MAT002

14.77

M128865

2.77

M129972

12

16

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____


Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					



DESIGN <i>LE</i>	DRAWN BY <i>LE</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>PH</i>	APPROVED <i>[Signature]</i>	DRAWING NO. D3573	REV. A SHEET 1 OF 4
DATE 07.02.19	TITLE ADAPTER	SCALE 1:1	
REV A	DATE 07.02.19	DESCRIPTION NEW ISSUE	


RELEASED
07.03.22

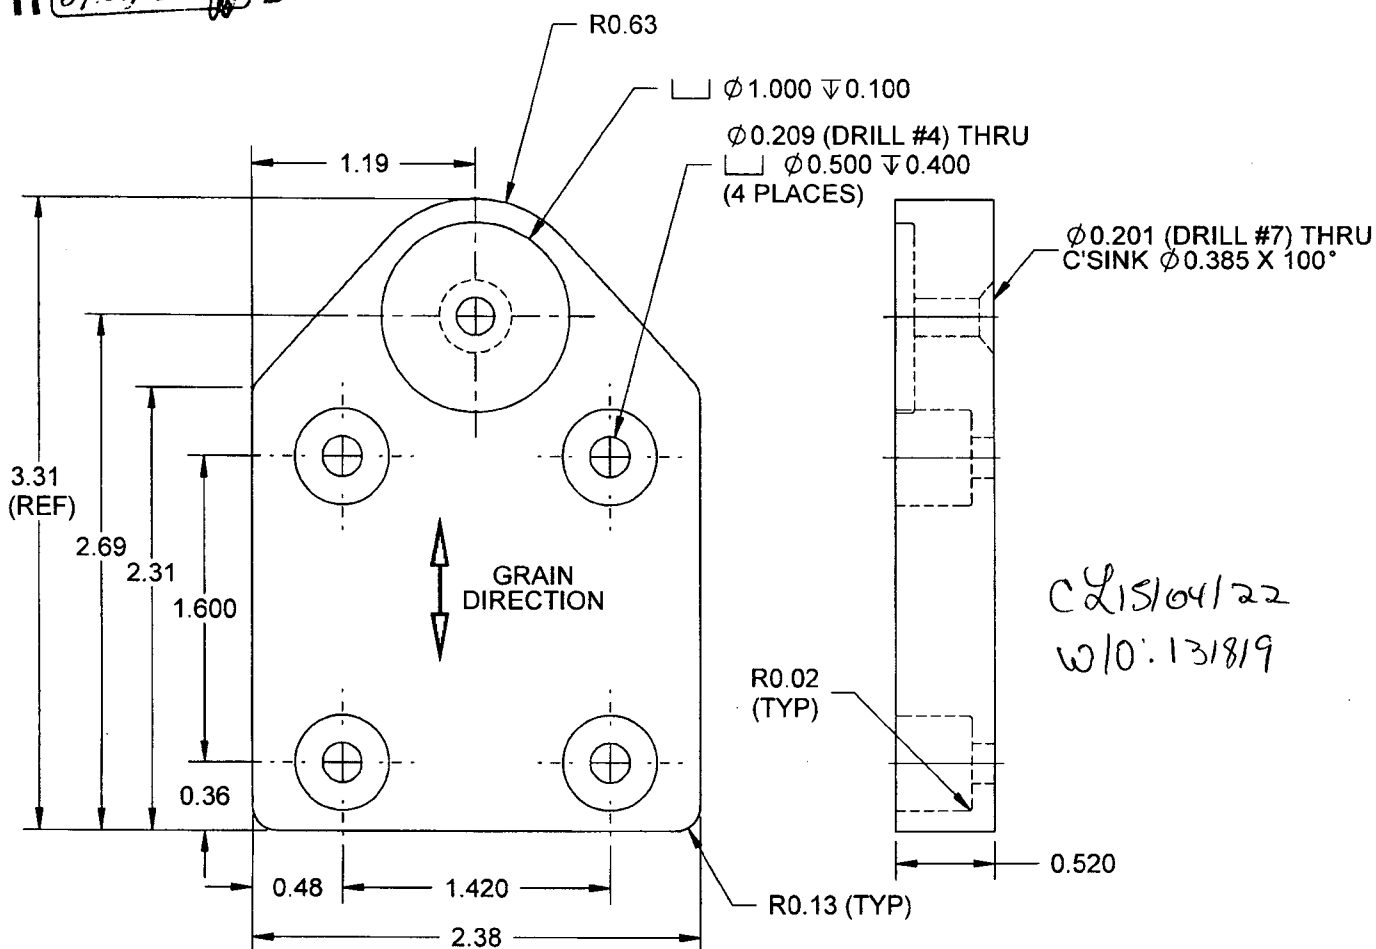

D3573-1 ADAPTER

NOTES:

- 1) MATERIAL: 6061-T6 (OR T651/T6510/T6511/T62) ALUMINUM BAR
PER QQ-A-225/8 OR QQ-A-200/8 OR AMS 4117/4128/4115/4116 OR AMS 4160
(REF DART SPEC M6061T6B)
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
POWDER COAT "GREY SANDTEX" (4.3.5.6) PER DART QSI 005 4.3
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) IDENTIFY WITH DART P/N "D3573-1" USING FINE POINT PERMANENT INK MARKER
- 5) ALL DIMENSIONS ARE IN INCHES UNLESS OTHERWISE NOTED
- 6) BREAK ALL SHARP EDGES 0.005 TO 0.010 MAX




COPYRIGHT © 2007 BY DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

DART

DESIGN <i>LE</i>	DRAWN BY <i>LE</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>PH</i>	APPROVED <i>[Signature]</i>	DRAWING NO. D3573	REV. A SHEET 2 OF 4
DATE 07.02.19		TITLE ADAPTER	SCALE 1:1

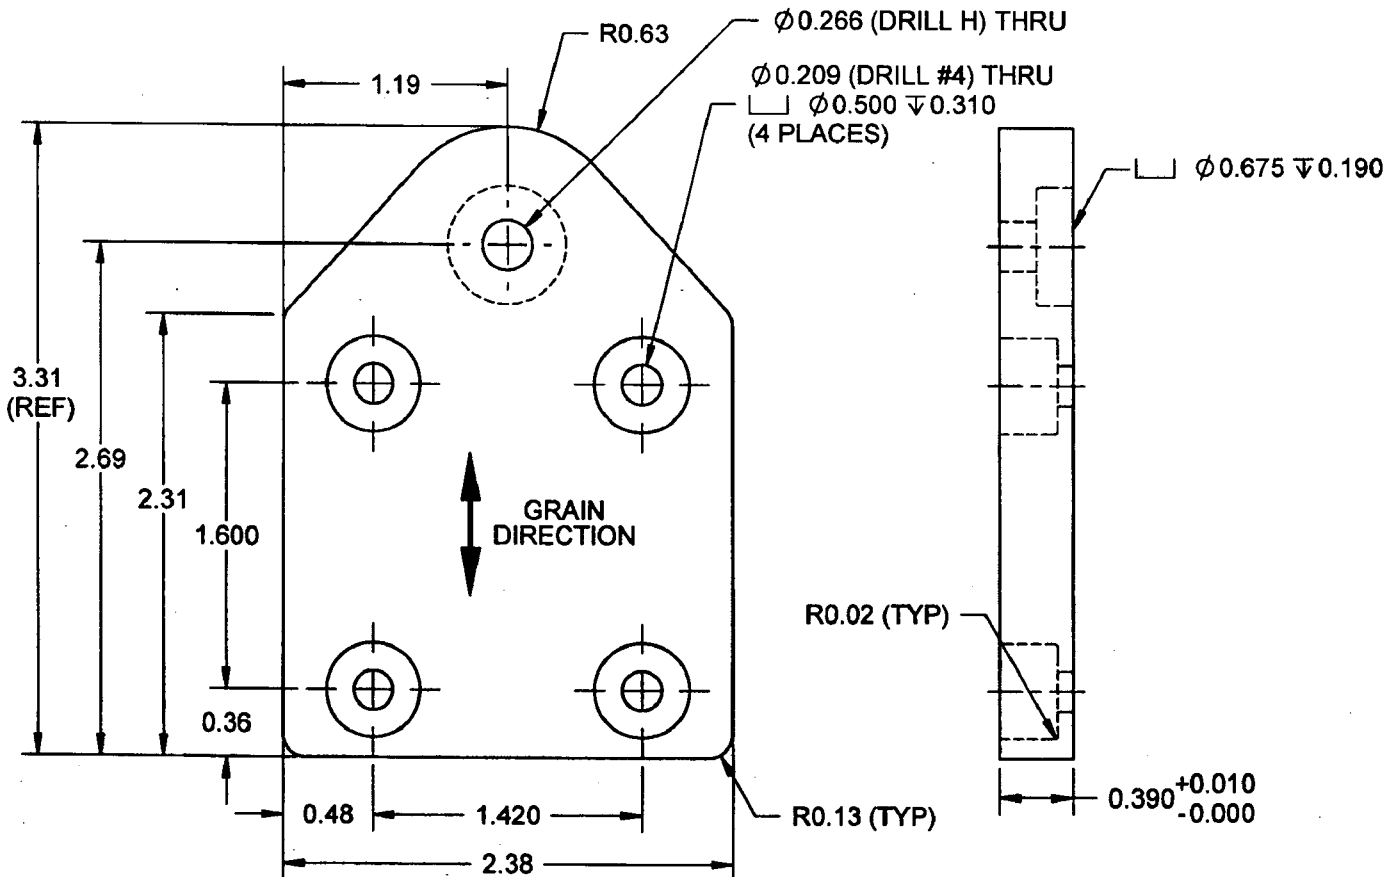RELEASED
07.04.02**D3573-3 ADAPTER****NOTES:**


- 1) MATERIAL: 6061-T6 (OR T651/T6510/T6511/T62) ALUMINUM BAR
PER QQ-A-225/8 OR QQ-A-200/8 OR AMS 4117/4128/4115/4116 OR AMS 4160
(REF DART SPEC M6061T6B)
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
POWDER COAT "GREY SANDTEX" (4.3.5.6) PER DART QSI 005 4.3
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) IDENTIFY WITH DART P/N "D3573-3" USING FINE POINT PERMANENT INK MARKER
- 5) ALL DIMENSIONS ARE IN INCHES UNLESS OTHERWISE NOTED
- 6) BREAK ALL SHARP EDGES 0.005 TO 0.010 MAX

COPYRIGHT © 2007 BY DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

DART

DESIGN <i>LE</i>	DRAWN BY <i>LE</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>PH</i>	APPROVED <i>[Signature]</i>	DRAWING NO. D3573	REV. A SHEET 3 OF 4
DATE 07.02.19		TITLE ADAPTER	SCALE 1:1

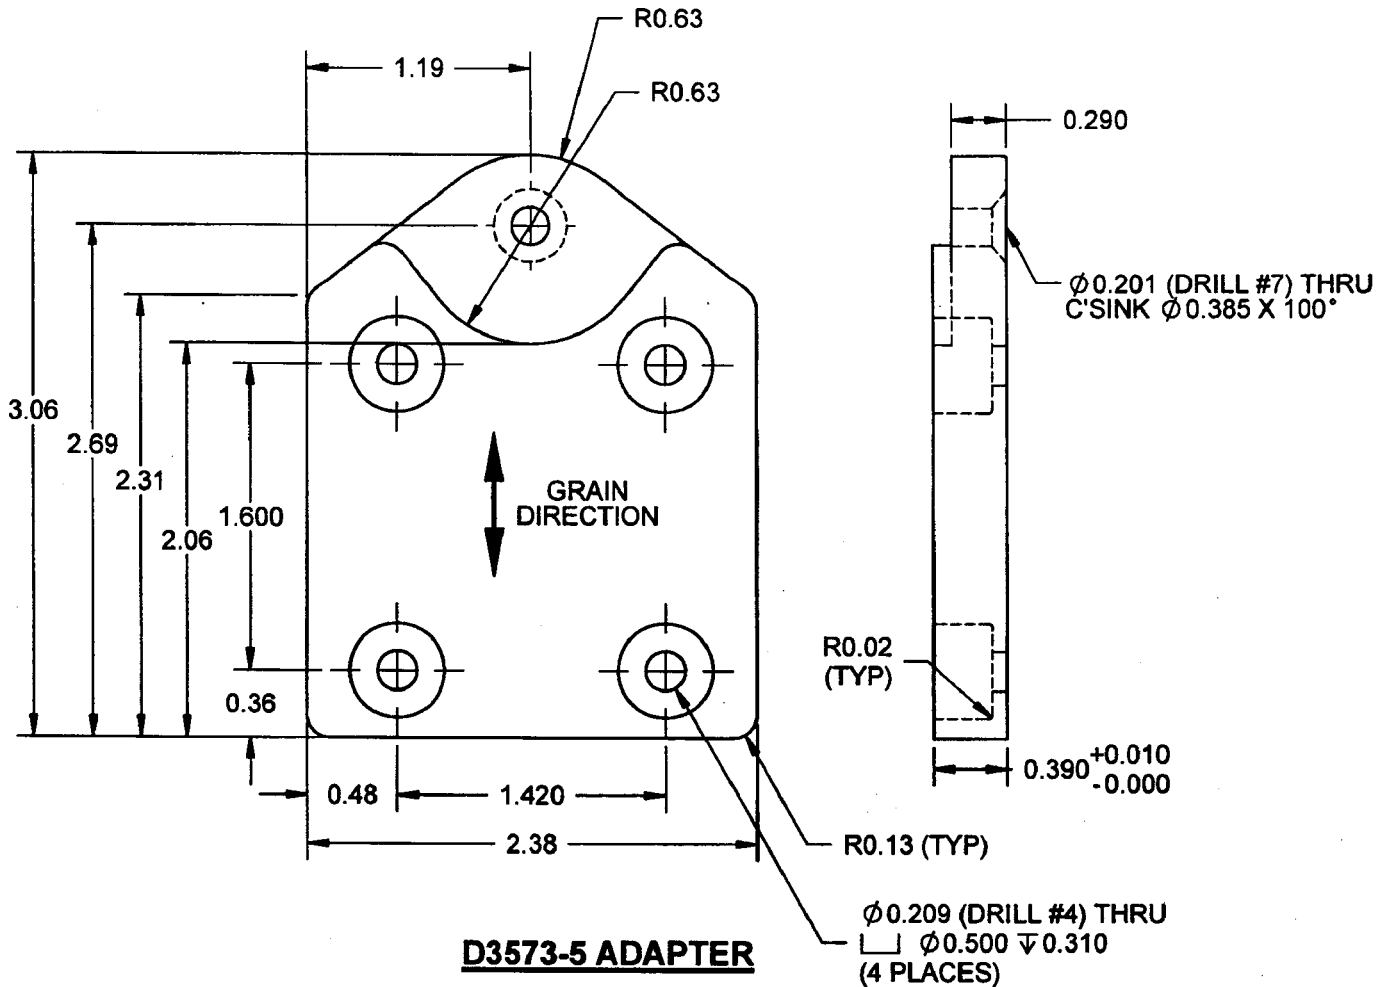RELEASED
07.04.02**NOTES:**

- 1) MATERIAL: 6061-T6 (OR T651/T6510/T6511/T62) ALUMINUM BAR
PER QQ-A-225/8 OR QQ-A-200/8 OR AMS 4117/4128/4115/4116 OR AMS 4160
(REF DART SPEC M6061T6B)
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
POWDER COAT "GREY SANDTEX" (4.3.5.6) PER DART QSI 005 4.3
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) IDENTIFY WITH DART P/N "D3573-5" USING FINE POINT PERMANENT INK MARKER
- 5) ALL DIMENSIONS ARE IN INCHES UNLESS OTHERWISE NOTED
- 6) BREAK ALL SHARP EDGES 0.005 TO 0.010 MAX


COPYRIGHT © 2007 BY DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.



DESIGN <i>LE</i>	DRAWN BY <i>LE</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>PH</i>	APPROVED <i>[Signature]</i>	DRAWING NO. D3573	REV. A SHEET 4 OF 4
DATE 07.02.19	TITLE ADAPTER		SCALE 1:1

RELEASED
07.04.02

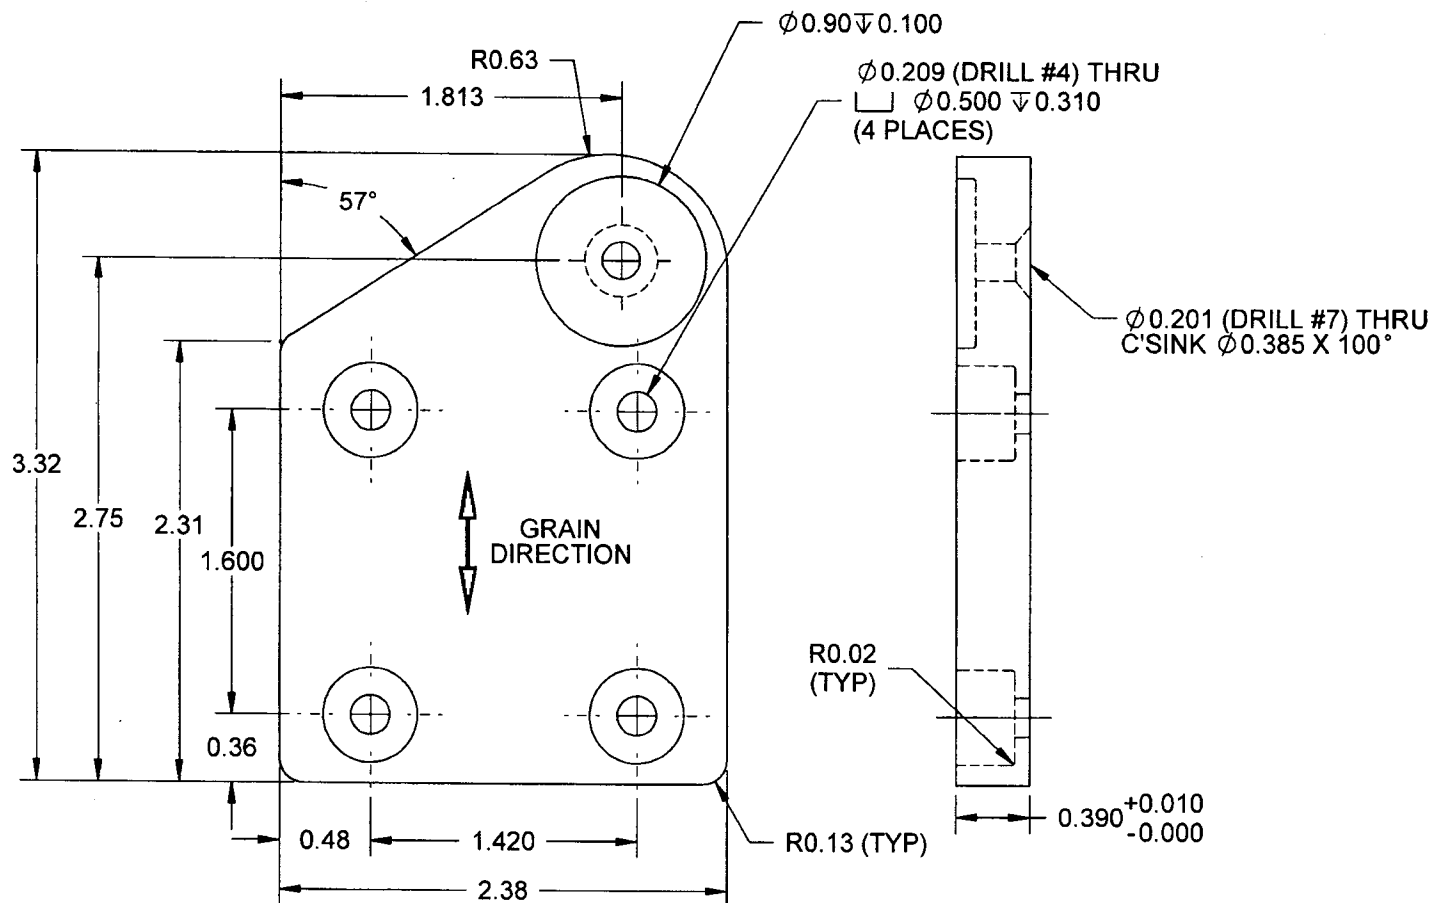

D3573-7 ADAPTER (SHOWN)
D3573-8 ADAPTER (OPPOSITE)

NOTES:

- 1) MATERIAL: 6061-T6 (OR T651/T6510/T6511/T62) ALUMINUM BAR
PER QQ-A-225/8 OR QQ-A-200/8 OR AMS 4117/4128/4115/4116 OR AMS 4160
(REF DART SPEC M6061T6B)
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
POWDER COAT "GREY SANDTEX" (4.3.5.6) PER DART QSI 005 4.3
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) IDENTIFY WITH DART P/N "D3573-7/-8" USING FINE POINT PERMANENT INK MARKER
- 5) ALL DIMENSIONS ARE IN INCHES UNLESS OTHERWISE NOTED
- 6) BREAK ALL SHARP EDGES 0.005 TO 0.010 MAX



COPYRIGHT © 2007 BY DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

DART AEROSPACE LTD		Work Order:	131819
Description: Adapter		Part Number:	D3573-1
Inspection Dwg: D3573 Rev: A		Page 1 of 1	

FIRST ARTICLE INSPECTION CHECKLIST

☒ First Article ☐ Prototype

Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
3.31	+/-0.030	3.310	✓		VERN	PHO-12
2.69	+/-0.030	2.689	✓		"	"
2.31	+/-0.030	2.31	✓		"	"
1.600	+/-0.010	1.600	✓		"	"
0.36	+/-0.030	.355	✓		"	"
1.19	+/-0.030	1.186	✓		"	"
2.38	+/-0.030	2.373	✓		"	"
1.420	+/-0.010	1.422	✓		"	"
0.48	+/-0.030	.475	✓		"	"
R0.63	+/-0.030	.630	✓		Rad G	
R0.13	+/-0.030	.130	✓		"	
R0.02	+/-0.030	.020	✓		"	
Ø0.209	+0.005/-0.001	.210	✓		VERN	PHO-12
Ø0.201	+0.005/-0.001	.202	✓		"	"
0.520	+/-0.010	.520	✓		"	"
Ø0.500 x 0.400	+/-0.010	.500 x .399	✓		"	"
Ø1.000 x 0.100	+/-0.010	1.001 x .099	✓		"	"

Measured by:	DAS 40 9-89	Audited by:	DA 08 9-89	Prototype Approval:	N/A
Date:	15/05/07	Date:	15/05/07	Date:	N/A

Rev	Date	Change	Revised by	Approved
A	07.04.04	New Issue	KJ/JLM	
